

**HOMES 4 WILTSHIRE  
PROJECT PLAN (TIMELINE)**








**APPENDIX A**

				<b>YEAR 1</b>									
TASK NAME	DURATION	START	FINISH	Nov-06	Dec-06	Apr-07	May-07	Jun-07	Aug-07	Sep-07	Oct-07	Nov-07	Feb-08
	<b>17 wks</b>	<b>5.11.06</b>	<b>1.3.08</b>										
Appoint lead officers from each District Council	4 wks	5.11.06	4.12.07										
Develop draft policy	26 wks	4.12.07	11.6.07										
Consultation ( Members in principle, Partners, Customers)	10 wks	11.6.07	21.8.07										
Appoint PM and Account holder	3 wks	21.8.07	10.9.07										
Apply for Funding	5 wks	10.9.07	12.10.07										
Develop ICT specification	12 wks	11.6.07	3.9.07										
Full CBL Policy	18 wks	12.10.07	18.2.08										
Develop marketing and Promotion strategy	16 wks	12.11.07	1.3.08										
Monitoring and Evaluation Strategy	16 wks	12.11.07	1.3.08										
<b>Implementation</b>	<b>28 wks</b>	<b>18.2.08</b>	<b>1.9.08</b>										
Procure ICT	16 wks	18.2.08	9.6.08										
System Testing	5 wks	9.6.08	14.7.08										
Staff Training	4 wks	9.6.08	7.7.08										
Data Conversion ( Common Housing Register)	8 wks	7.7.08	1.9.08										
Marketing	22 wks	1.3.08	22.7.08										
<b>Launch</b>	<b>33 wks</b>	<b>11.8.08</b>	<b>31.3.09</b>										
<b>Launch 1 ( KDC, SDC &amp; WWDC)</b>	4 wks	1.9.08	29.9.08										

**HOMES 4 WILTSHIRE  
PROJECT PLAN (TIMELINE)**


**APPENDIX A**

<b>Launch 2 ( NWDC)</b>	<b>12 wks</b>	<b>10.1.09</b>	<b>31.3.09</b>										
<b>Monitoring and Evaluation 1</b>	<b>52 wks</b>	<b>1.9.08</b>	<b>1.9.09</b>										
<b>Widening Partnership (SBC)</b>	<b>52 wks</b>	<b>1.4.09</b>	<b>1.4.10</b>										

	Phase
	Stage completed
	Stage in process
	Not started
	Expansion
	Finish to start
	Start to start

# HOMES 4 WILTSHIRE PROJECT PLAN (TIMELINE)

APPENDIX A

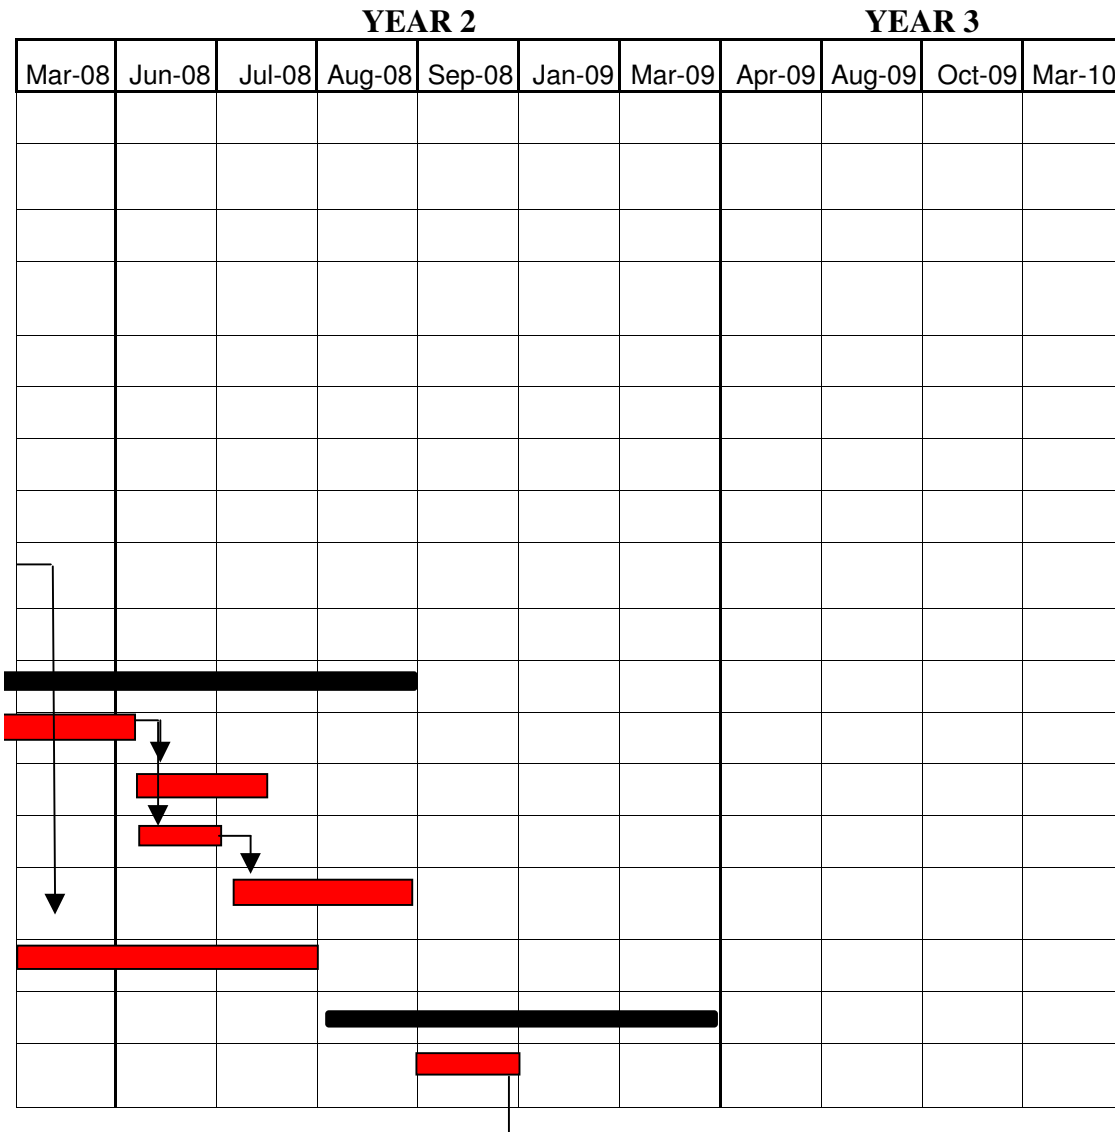

**HOMES 4 WILTSHIRE  
PROJECT PLAN (TIMELINE)**

**APPENDIX A**

