Appendix 4
Workplace Transformation Programme
Outline Master Programme
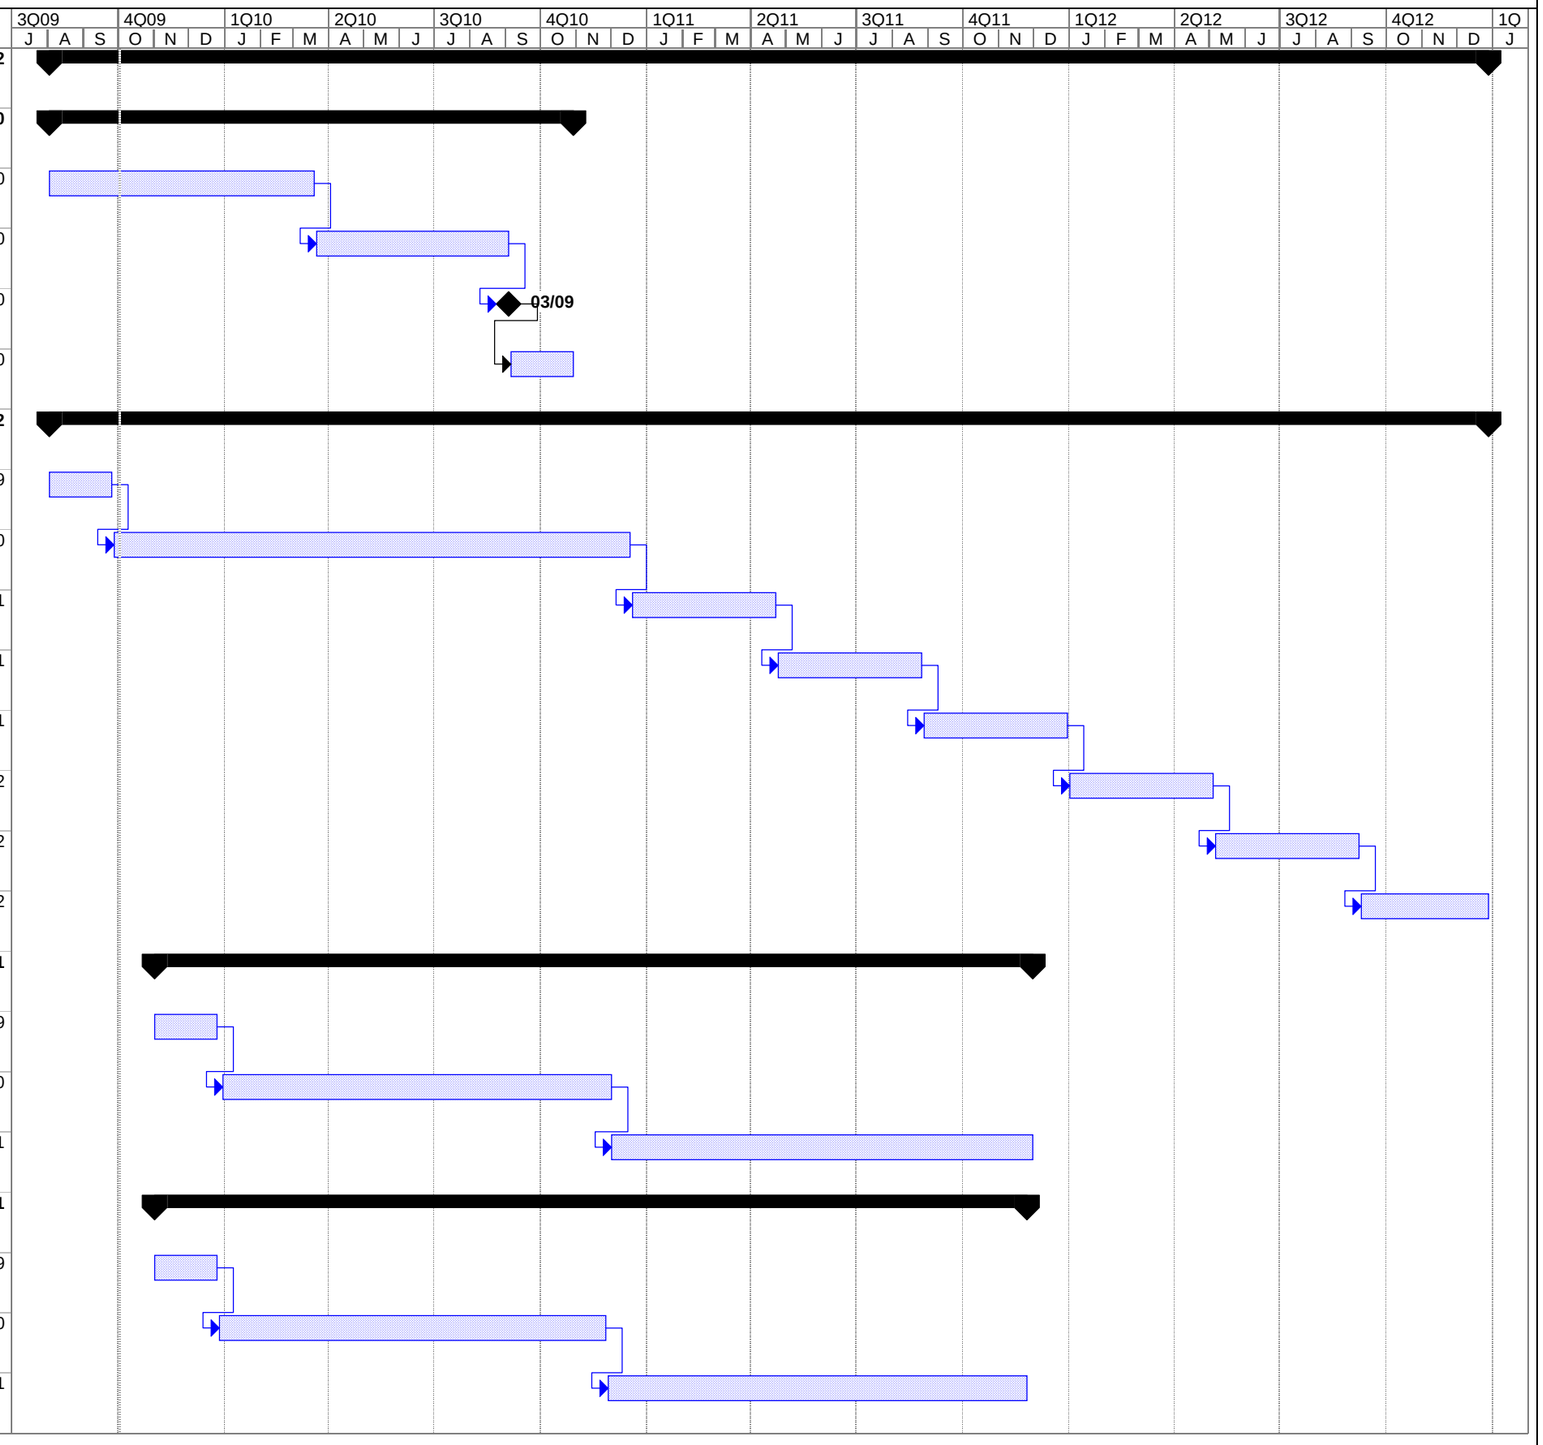
ID		Task Name	Duration	Start	Finish
1		**Projects**	**178 wks**	**Mon 03/08/09**	**Fri 28/12/12**
2		**Bourne Hill, Salisbury**	**65 wks**	**Mon 03/08/09**	**Fri 29/10/10**
3		Construction	33 wks	Mon 03/08/09	Fri 19/03/10
4		Fit out & retrofit works	24 wks	Mon 22/03/10	Fri 03/09/10
5		Building operational	0 wks	Fri 03/09/10	Fri 03/09/10
6		Relocations	8 wks	Mon 06/09/10	Fri 29/10/10
7		**Trowbridge**	**178 wks**	**Mon 03/08/09**	**Fri 28/12/12**
8		Pre-project	8 wks	Mon 03/08/09	Fri 25/09/09
9		Confirm Design & Procure	64 wks	Mon 28/09/09	Fri 17/12/10
10		Construction Phase 1	18 wks	Mon 20/12/10	Fri 22/04/11
11		Construction Phase 2	18 wks	Mon 25/04/11	Fri 26/08/11
12		Construction Phase 3	18 wks	Mon 29/08/11	Fri 30/12/11
13		Construction Phase 4	18 wks	Mon 02/01/12	Fri 04/05/12
14		Construction Phase 5	18 wks	Mon 07/05/12	Fri 07/09/12
15		Construction Phase 6	16 wks	Mon 10/09/12	Fri 28/12/12
16		**Devizes**	**108.6 wks**	**Mon 02/11/09**	**Wed 30/11/11**
17		Pre-project	8 wks	Mon 02/11/09	Fri 25/12/09
18		Confirm Design & Procure	48 wks	Thu 31/12/09	Wed 01/12/10
19		Construction	52 wks	Thu 02/12/10	Wed 30/11/11
20		**Chippenham**	**108 wks**	**Mon 02/11/09**	**Fri 25/11/11**
21		Pre-project	8 wks	Mon 02/11/09	Fri 25/12/09
22		Confirm Design & Procure	48 wks	Mon 28/12/09	Fri 26/11/10
23		Construction	52 wks	Mon 29/11/10	Fri 25/11/11
